

FINAL REPORT

YEMEN SMALLHOLDER AGRICULTURAL PRODUCTIVITY RESTORATION
AND ENHANCEMENT PROJECT (SAPREP)

Report by:

GHADAQ FOR DEVELOPMENT

Submitted to:

Food and Agriculture organization of the UN (FAO)

Project Name	Smallholder Agricultural Production Restoration and Enhancement Project (SAPREP)
Letter of Agreement number (reference)	OSRO/YEM/407/WBK
Date of entry into force of LoA	25 March 2018
End date of LoA first phase	31 December 2018
End date of LoA extension phase	31 October 2019
Reporting period	March 2018- October 2019
Submitted by (name of the responsible officer)	Dr Abdul Gabbar Al-Kirshi



CONTENTS	PAGE
1. INTRODUCTION	3
2. PURPOSE AND DELIVERABLE OUTPUTS	3
a. OUTPUTS	3
b. OUTPUTS INDICATORS OF THE FIRST PHASE	4
3. RESPONSIBILITIES	4
4. TARGETED BENEFICIARIES	4
5. IMPLEMENTATION OF ACTIVITIES OF THE FIRST PHASE	6
a. SEQUENCE THE CONDUCTED ACTIVITIES	6
b. OUTPUTS, ACTIVITIES, SUB- ACTIVITIES AND ACHIEVEMENTS	8
6. ACTIVITIES IN THE EXTENSION PHASE	15
OUTPUTS INDICATORS OF THE FIRST PHASE	15
7. CHALLENGES ENCOUNTERED THROUGH THE IMPLEMENTATION OF THE ACTIVITIES	18
8. LESSONS LEARNED	18
9. DOCUMENTATIONS	19

1. INTRODUCTION

GHADAQ for Development and FAOYEMEN signed a Letter of Agreement (LoA) called: "Provision of Services for Distribution of Emergency Agricultural Inputs to IDPs and Host Communities in Hodeidah Governorate". The services are under the framework of the project "YEMEN SMALLHOLDER AGRICULTURAL PRODUCTIVITY RESTORATION AND ENHANCEMENT PROJECT" financed by the World bank and implemented by FAOYEMEN.

The project development objective (PDO) focuses on increasing the use of productivity and nutrition to enhance agricultural practices by smallholders in **Assuchnah** and **Bait Alfaqeeh** districts, Hudaidah governorate. This will be achieved through restoring and enhancing access to agriculture inputs, providing specific investments and technical assistance to improve agriculture yields and nutritional value and upgrade diversify agriculture and livestock production and marketing.

In the extension phase April -October 2019 activities in **Alzaydiah** district have been added to be supervised and items to be distributed by Ghadaq Organisation.

Under the LoA conditions signed between the FAO and GHADAQ the activities have targeted poor and food-insecure households as well as beneficiaries affected by the conflict. The following groups have been given priorities:

- (i) Landless farmers with no or few livestock;
- (ii) Sharecroppers and casual workers;
- (iii) Smallholder farmers with less than 1.3 ha of land;
- (iv) Women-headed households;
- (v) Conflict affected households, returnees and IDPs.

2. PURPOSE AND DELIVERABLE OUTPUTS

The purpose of the activities is to restore and increase the use of productivity and nutrition enhancing agricultural practices by smallholders in targeted project areas of As- Sukhnah, Alzaydia and Bayt AL- Faqeeh districts. This will be realised through livelihood assistance in terms of training, awareness building and technical support by distribution of agricultural inputs like dairy equipment, live animals, animal feed, poultry and cereal and forage seeds.

About 11,176 Households most vulnerable and food insecure households in As -Sukhnah and Bayt AL- Faqeeh districts will make use of the current ongoing interventions.

a. OUTPUTS

1. Training and capacity development sessions to 100% of the targeted households (one training sessions for each beneficiary group) on topics related to restocking, dairy and crop production.
2. Distribution of livelihoods assets (sheep and goats) and inputs (forage and cereal seeds, animal feed concentrate, feed blocks, poultry, and dairy

equipment) to beneficiaries in the districts of **As- Sukhnah, Bayt- AL Faqeeh and Alzaydia** of Hodeidah governorate. FAO inputs are expected to be delivered in good safety and timely manner to poor households in a maximum period of 9 months from the entry into force of the Letter of Agreement (LOA).

b. OUTPUTS INDICATORS OF THE FIRST PHASE

- 160 households supported with livestock inputs.
- 238 households supported with poultry inputs.
- 400 households supported with forage seeds inputs
- 2,143 households supported with dairy equipment and 200 HHs supported with chopper forage machines.
- 8,035 HHs supported with cereal seeds (sorghum and millet)
- Number of training sessions conducted on the five areas of intervention (livestock, poultry, dairy and forage and cereal seeds) to 100% of the targeted households (based on the input each HH is receiving).
- Number of households aware of the complaints and feedback mechanism.
- Number of community committees established.

3. RESPONSIBILITIES


GHADAQ has taken the following actions under direct overall supervision of the Director of Agricultural Office in the governorate:-

- Prepare distribution plan in each location complete with names of the beneficiaries;
- Arrangements to contact all beneficiaries
- Coordinate with the suppliers to identify and fix the places in each district as distribution points for livestock, poultry, animal feed, dairy equipments and forage and cearyl seeds.
- In coordination with supplier, local authorities at district, Director of Agricultural Office in governorate carry out distribution of all inputs to the targeted beneficiaries.
- Prepare the distribution names lists containing the same agreed lists of beneficiaries and containing the following data: the name of beneficiary, the village name, Sub-district (Ozlah) name, District name, Quantity of inputs received, Stamp (Fingerprint) and the bottom of each list should include the signature and stamp of director of local authority, director of agricultural office in the districts and governorate.


4. TARGETED BENEFICIARIES

Map 1 and map 2 reflect the targeted districts, sub districts and villages. Table 1 shows the actual direct targeted sub districts. We have worked in 5 sub districts and 11 training and distribution points. The type of the training distribution points are mostly

schools. In Some cases, we have to select Al-Aqel houses as distribution points. The due figures of targeted sub districts and villages of As-Suchknah district are reflected in map 2 and table 1.

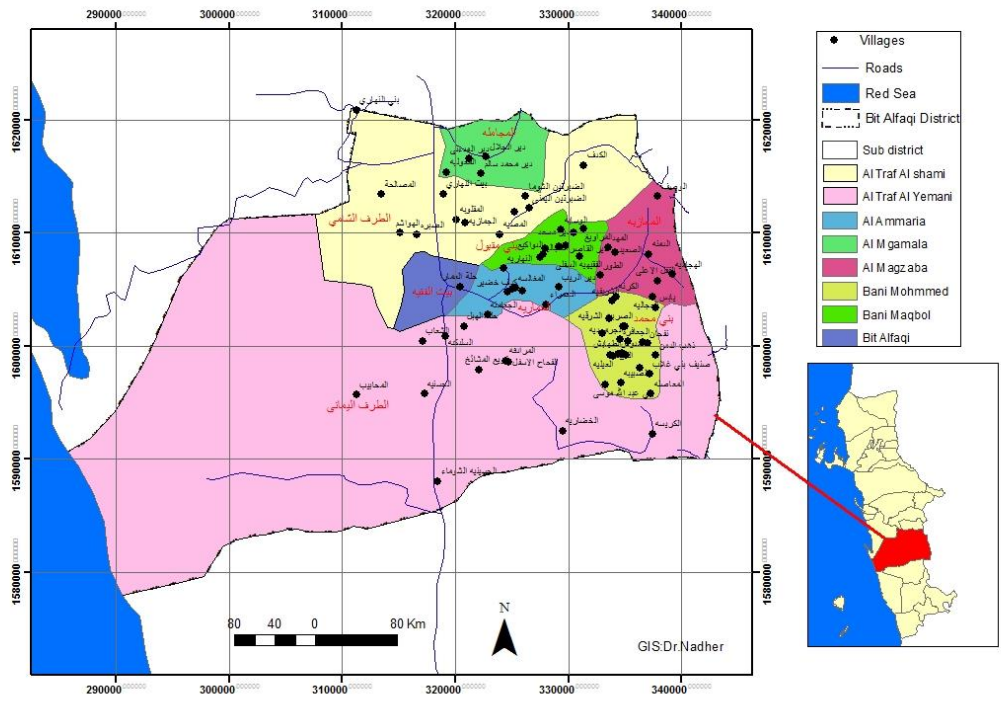

Map 1: Bait alfaqeeh, showing the district, the sub districts and the villages targeted by the FAO agricultural distributed inputs

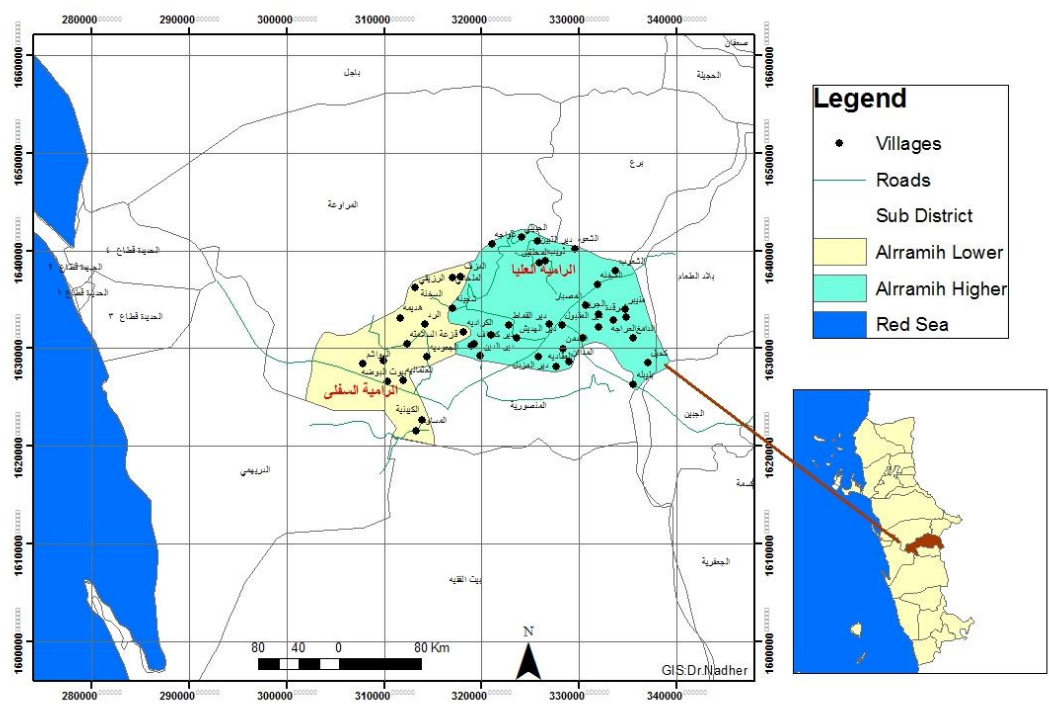

Map 2: As-Sucknah, showing the district, the sub districts and the villages to by the FAO agricultural distributed inputs

Table 1: District, Sub districts and training and distribution points (first phase place and type)

Districts	Sub district	Training and distribution points	Place type	
Bait Alfaqeeh	Al—A'amarah ¹	Kadf Khudaeer	school	
	Bani Mohammed	Alkarnah	school	
	Bani Maqbool	Deer Alqaser	school	
	Altaraf Al-Yamany		Alsulaikyia	Alaqel house
			Meeyah	Alaqel house
			Qwaie'e Al-Sharqeeiah	school
			Almaradifah	school
			Bait Alhalaj	school
	Altaraf Al-Shamy		Al-Musiah	school
			Taraf Alnu'umy	school
		Al-Ma'waliah	school	
Assukhnah	Altaraf Al-Shamy	Sha'wah	Alsalam School	
		Almahtah (Almafraaq)	Albachash center	
	Alramiah Assuflah	Bait Albuttah	Alwahdah School	


5. IMPLEMENTATION OF ACTIVITIES OF THE FIRST PHASE

a. SEQUENCE THE CONDUCTED ACTIVITIES:


- Letters from the FAO representative in Yemen addressed to governor of AlHudeidah and to the director of the National Authority for Coordination of Humanitarian Affairs in AlHudeidah have been delivered in Mach 2018;
- Starting the work immediately after receiving positive response to the above mentioned letters by contacting:
 - The head of the Tehama Development Authority (TDA),
 - The office of the governor of AlHudeidah;
 - Receiving approval and letters from the governor of Hudaidah ordering responsible figures on the governorate and at districts levels to support and help "Ghadaq for Development" in its current activities. The letters of the governor were addressed to:
 - The director of security in AlHudeidah governorate;
 - (a) The general director of Bayt Al-Faqeeh district;
 - (b) The general director of Alsukhuna district;
 - Appointing a general technical supervisor and a general coordinator and training supervisor

- Selection and contract the district coordinators for Bayt Al-Faqeeh and for Alsukhuna with the following main tasks:
 - (a) Help by contacting of local authorities and explain to them the purpose of the ongoing activities
 - (b) Help by selection of the surveyors teams in both districts;
 - (c) Help by training the selected teams on how to deal with the questionnaires;
 - (d) Day by day follow up the field work and receiving the forms filled and coming from every member of the field team, archive the forms, entering the data in the due lists;
 - (e) Weekly report to the general coordinator and training supervisor.
- Selection of surveyors;
- Training the selected surveyors and giving them clear instructions on how to start the work, what of lists of beneficiaries every surveyors should take with him and to which villages he should go;
- Giving the surveyors contacts of the head of every village "A'qel" to contact and inform him about the purpose of the visit.

Map 3 and map 4 show the training and distribution points in the sub districts and the villages of the two districts. In Bait –Al-Faqeeh there were eleven training and distribution points spread in five sub districts. In As-Suchnah there were three training and distribution points in the two main sub districts.

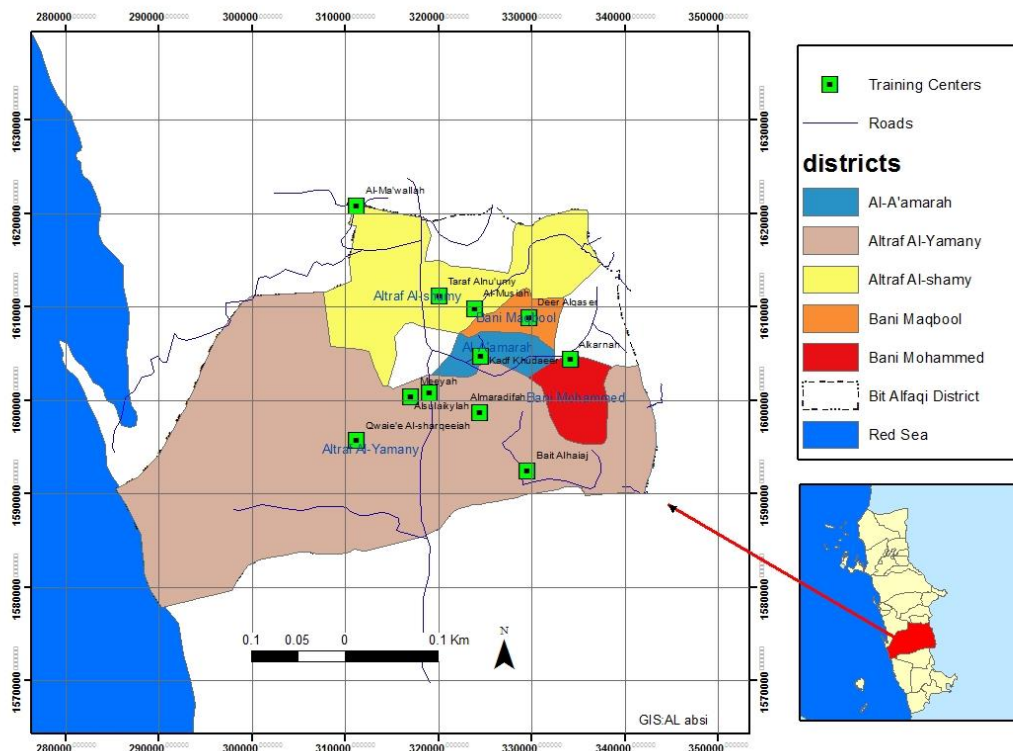

Map 3: Bait alfaqeeh, showing the training and distribution points in the sub districts and the villages

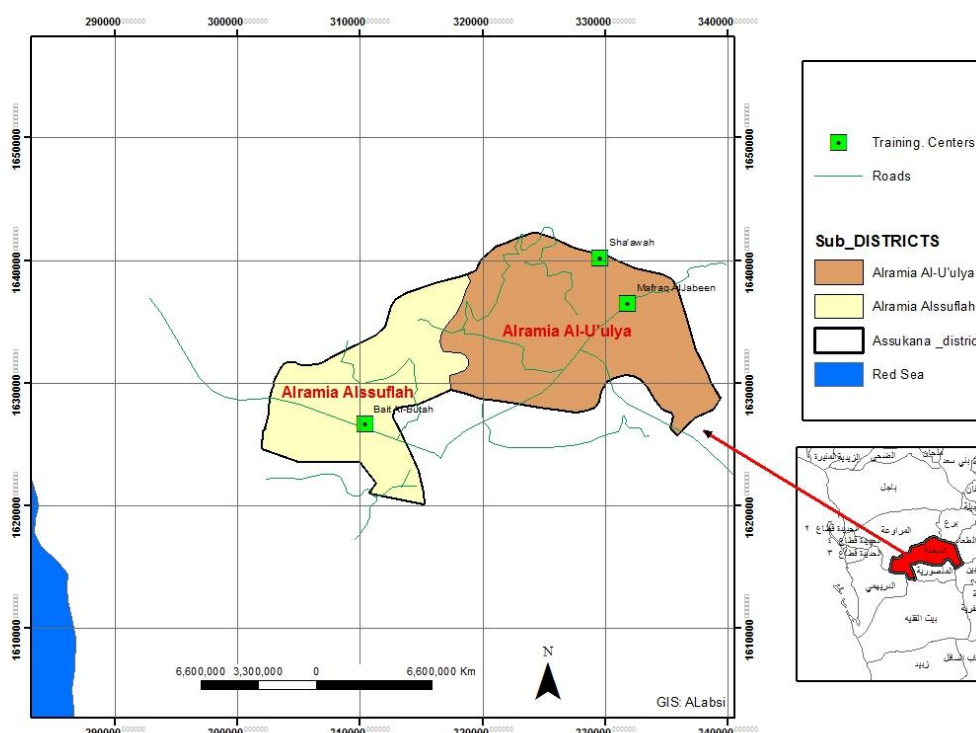

Map 4: Assuchnah, showing the training and distribution points in the sub districts and the villages

b. OUTPUTS, ACTIVITIES, SUB- ACTIVITIES AND ACHIEVEMENTS

Table 2 reflects the activities conducted and achievements as stand by the end of July 2018. The percent achievements for training and distribution so far reached mostly 100 % as shown in the table.

Table2: Outputs, activities, Sub- activities and percent achievements in the first phase April- December 2018

Outputs	Activities	Sub-activities	Achievements (%)
Training of BF's and Distribution of Sorghum seeds to 2300 beneficiaries Bait -Alfaqeeh	1. Receiving and store of 46 MT sorghum in Bait alfaqeeh 2. Training of beneficiaries 3. Distribution of items.	1. Starting preparation for training and distribution by making contracts with trainers.	100
Training of BF's and Distribution of Millet seeds to 2170 beneficiaries Bait -Alfaqeeh	1. Receiving and store of 43.4 MT Millet in Bait alfaqeeh 2. Training of beneficiaries 3. Distribution of items	2. Selection of distributors (Females and males) 3. Fixing the distribution points and distribution stores.	100
Training of BF's and Distribution of Sorghum seeds to 1900 beneficiaries As-Suchnah	1. Receiving and store of 38 MT sorghum in Assuchnah 2. Training of beneficiaries 3. Distribution of items	4. Conducting the training and distribution activity	100

Training of BFs and Distribution of Millet seeds to 1665 beneficiaries As-Suchnah	<ol style="list-style-type: none"> 1. Receiving and store of 33.3 MT Millet in Assuchnah 2. Training of beneficiaries 3. Distribution of items 		100
Training of BFs and distribution of forage seeds to 200 beneficiaries Bait -Alfaqeeh	<ol style="list-style-type: none"> 1. Receiving and store of 1 MT cowpea and 4 MT Bani forage seeds in Assuchnah Districts 2. Training of beneficiaries 3. Distribution of items 		100
Training of BFs and distribution of forage seeds to 200 beneficiaries As-Suchnah	<ol style="list-style-type: none"> 1. Receiving and store of cereal seeds in Bait afaqeeh District 2. Training of beneficiaries 3. Distribution of items 		100
Training of BFs and distribution of small ruminants (Sheep and goats) in Assuchnah for 80 beneficiaries As-Suchnah	<ol style="list-style-type: none"> 1. Receiving and keeping of 400 small ruminants (Sheep and goats) in Assuchnah 2. Training of beneficiaries 3. Distribution of items 		100
Training of BFs and distribution of small ruminants (Sheep and goats) in Assuchnah for 80 beneficiaries Bait -Alfaqeeh	<ol style="list-style-type: none"> 1. Receiving of 400 small ruminants (Sheep and goats) in Bait alfaqeeh 2. Training of beneficiaries 3. Distribution of items 		100
Training of BFs of beneficiaries and distribution of feed concentrate to 80 beneficiaries Bait -Alfaqeeh	<ol style="list-style-type: none"> 1. Receiving and keeping of 16 MT feed concentrate Assuchnah 2. Training of beneficiaries 3. Distribution of items 		100
Training of BFs of beneficiaries and distribution of feed concentrate to 80 beneficiaries Bait -Alfaqeeh	<ol style="list-style-type: none"> 1. Receiving and keeping of 16 MT feed concentrate Bait Alfaqeeh 2. Training of beneficiaries 3. Distribution of items 		100

In table 3 we can see male and female headed HHs and number of HHs replaced during the verification phase. We received already registered lists for Poultry, live animal and animal feed and for cereal seeds. We have conducted new registration for dairy inputs, chopper forage machines and forage seeds.

Table 3: Male and female headed households and number of HHs replaced during the verification phase

Districts	Poultry				
	M- headed HHs	F-headed HHs	Total HHs	Verified HHs	# of HHs replaced
Bait Alfaqeeh	100	19	119	119	14
Alsukhnah	56	63	119	119	15
	156	82	238	238	
Districts	Live animals & Animal feed				
	M- headed HHs	F-headed HHs	Total HHs	Verified HHs	# of HHs replaced
Bait Alfaqeeh	43	37	80	80	0
Alsukhnah	28	52	80	80	8
	71	89	160	160	
Districts	Cereal seeds (one list for each variety)				
	M- headed HHs	F-headed HHs	Total HHs	Verified HHs	# of HHs replaced
Bait Alfaqeeh	4100	301	4401	4455	225
Alsukhnah	3246	309	3555		96
	7346	610	7956		
Districts	Dairy inputs				
	M- headed HHs	F-headed HHs	Total HHs	Verified HHs	# of HHs replaced
Bait Alfaqeeh	1073	330	1403	1403	
Alsukhnah	478	238	716		
	1551	568	2119		
Districts	Chopper forage machine				
	M- headed HHs	F-headed HHs	Total HHs	Verified HHs	# of HHs replaced
Bait Alfaqeeh	79	20	99	99	
Alsukhnah	95	5	99		
	174	25	198		
Districts	Forage seeds				
	M- headed HHs	F-headed HHs	Total HHs	Verified HHs	# of HHs replaced
Bait Alfaqeeh	178	22	200		
Alsukhnah	169	41	200		
Total	347	63	400		

Table 4 reflects the male and female distributors and trainers in Bait Al-Faqeeh and Assuchnah districts.

Table 4: Male and female distributors and trainers in Bait Al-Faqeeh and Assuchnah

Districts	Type of distributors/ trainers			
	# of Female distributors	# of male distributors	# of Female trainers	# of male trainers
Bait Alfaqeeh	2	7	2	4
Alsukhnah	2	8	2	6
Total	4	15	4	10


Table5: Receiving and stationed of chopper machines Bait Alfaqeeh

Chopper machines NO	Stationed village	Sub district	# of BFs registered	New registered	At least Total # of BFs to make use of the machine
1	Bani Fatah	Ala'amarah	10	25	35
2	AlMahd	Alma'azibah	13	22	35
3	Al-Karanah	Bani Mohamaed	11	24	35
4	Deer Almadany	AlMajamelah	9	26	35
5	Hasy Mohamed	Altaraf Alshamy	12	23	35
6	Aldwakey	Bani Maqbool	9	26	35
7	Deer Alqaser	Bani Maqbool	6	29	35
8	Almahezerah	Bait alfaqeeh city	10	25	35
9	Al-Husainiah	Altaraf Aymany	14	21	35
10	Alkdadeef	Altaraf Aymany	15	20	35
Total			109	241	350


Table 6: Receiving and stationed of chopper machines Assuchnah

Chopper machines NO	Stationed village	Sub district	# of BFs registered	New registered	At least Total # of BFs to make use of the machine
1	Almahelateen	Alramiah	10	25	35
2	Almurrah	Alu'wlya	10	25	35
3	Deer Dawood	Alramiah Aleesta	10	25	35
4	Kuhail		10	25	35

5	Shujainah	Alramiah Alu'wlya	10	25	35
6	Mahel Ruwaid		10	25	35
7	Alqaza'ah	Alramiah Assufla	10	25	35
8	Albutah		10	25	35
9	Alkaibaniyah		10	25	35
10	Beyoot Alza'awer		10	25	35
Total			100	250	350

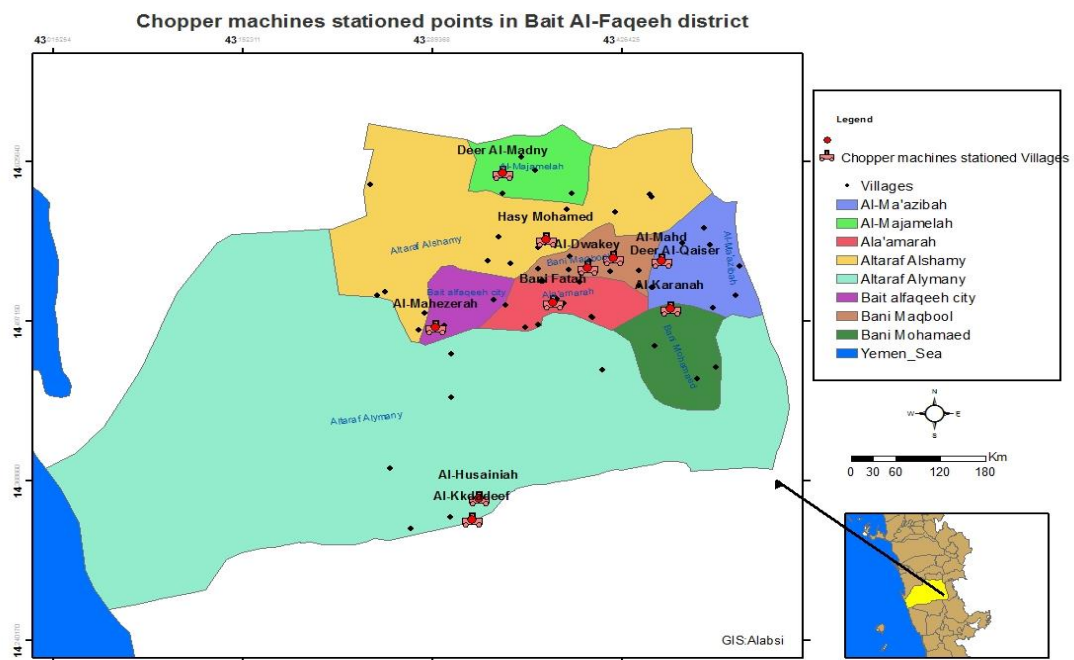

Map 5: Stationed points of chopper machines in Bait Alfaqeeh

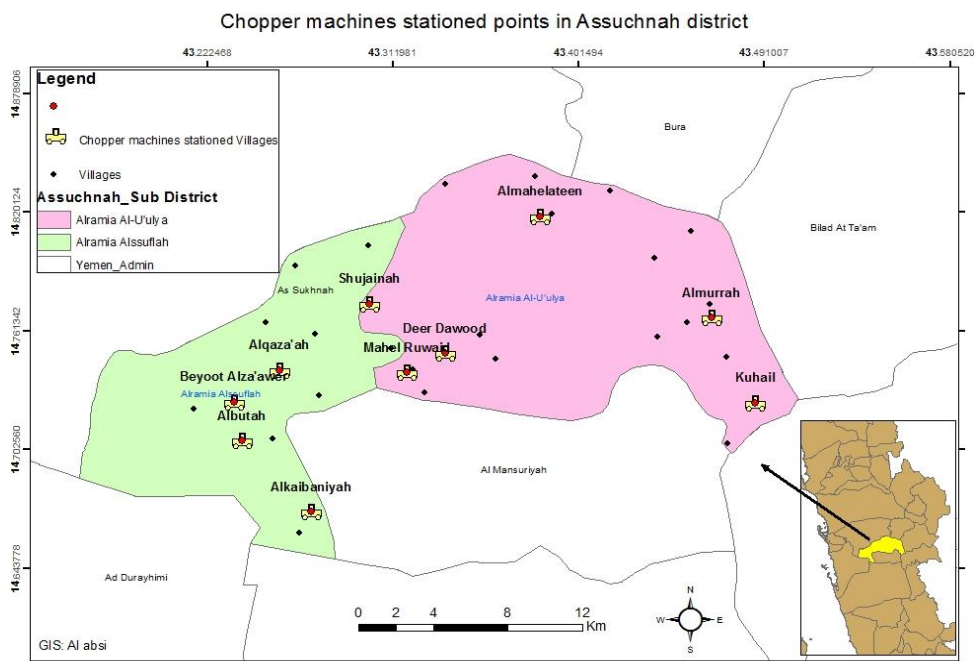

Map 5: Stationed points of chopper machines in Assuchnah

Table 7: Distribution of dairy equipment in Bait Alfaqeeh

#	Categories of milk production liter	# of beneficiaries produced in rain period	Dairy Equipment to be distributed Received Bait Alfaqeeh						
			Milk Can 20 ltr	Milk Can 10 ltr	Cream Can 5 ltr	Plastic Filters	Mini Dairy	Butter churn	Milk Buckets
1	5 to 10 liter	211			422	211			211
2	11 to 24 liter	988		1976	1976	2964			988
3	More than 25	197	197	394	394	591			197
		1396	197	2370	2792	3766	118	118	1396

- Total beneficiaries = 1428
- Total beneficiaries produced **milk** 5- 10 ltr = 211 . Every beneficiary of these category will receive 2 cream cans of 5 ltr, 1 plastic filter and 1 Milk buckets
- Total beneficiaries produced 11- 24 ltr = 988 . Every beneficiary of these category will receive 2 milk can of 10 ltr, 2 cream cans of 5 ltr, 3 plastic filter and 1 Milk bucket
- Total beneficiaries produced more than 25 ltr 197 . Every beneficiary of these category will receive 1 milk can of 20 ltr, 2 milk can of 10 ltr, 2 cream cans of 5 ltr, 3 plastic filter and 1 Milk buckets

Table 8: Distribution of dairy equipment in Assuchnah

#	Categories of milk production liter	# of beneficiaries produced in rain period	Dairy Equipment to be distributed Received Assuchnah						
			Milk Can 20 ltr	Milk Can 10 ltr	Cream Can 5 ltr	Plastic Filters	Mini Dairy	Butter churn	Milk Buckets
1	5 to 6 liter	125			250	125			125
2	7 to 18 liter	490		980	980	1470			490
3	More than 18 liter	100	100	200	200	300			100
		715	100	1180	1430	1895	60	60	715

- Total beneficiaries = 715
- Total beneficiaries produced **milk** 5- 6ltr = 125 . Every beneficiary of these category will receive 2 cream cans of 5 ltr, 1 plastic filter and 1 Milk buckets
- Total beneficiaries produced 7- 18 ltr = 490 . Every beneficiary of these category will receive 2 milk can of 10 ltr, 2 cream cans of 5 ltr, 3 plastic filter and 1 Milk buckets
- Total beneficiaries produced more than 18 ltr =100 . Every beneficiary of these category will receive 1 milk can of 20 ltr, 2 milk can of 10 ltr, 2 cream cans of 5 ltr, 3 plastic filter and 1 Milk buckets

6. ACTIVITIES IN THE EXTENSION PHASE

In the extension phase April- October 2019 the district **Alzaydiah** has been added to Ghadaq beside the former districts **Bait Alfaqeeh** and **Asuchnah**.

Table 9: Agricultural items distributed in the extension project phase

Gov.	District	live animal, animal feed and feed blocks				poultry inputs			
		# HHs	Quan. Heads	Feed concent rate 200kg/HH	feed block 10/HH	# HHs	Egg laying chicken	egg laying houses	chicken feed 7 kg/HH
Hudidah	Bait Alfaqeeh	60	300	12000	600	50	500	50	3500
	Alzaydiah	60	300	12000	600	50	500	50	3500
	Alsukhnah	60	300	12000	600	50	500	50	3500
Total	3	180	900	36000	1800	150	1500	150	10500

Gov.	District	Seed				Fodder chopper			The chopper machines have not been received
		Sorghum 20kg/HHs	Sorghum Variety	Millet 20 kg/HH	Cowpea 5kg/HH	# BHHs	# Chopper	# BHHs	
Hudidah	Bait Alfaqeeh	12000	Qaira'a	4000	4000	800	2	40	
	Alzaydiah	8000	Zeir	3000	2750	550	3	60	
	Alsukhnah	7000	Zeir	3000	2500	500	2	40	
Total	3	27000		10000	9250	1850	7	140	

Outputs indicators of the extension phase April – October 2019:

- 180 households supported with restocking inputs.
- 150 households supported with poultry inputs.
- 1850 HHs supported with cereal seeds (sorghum and millet)
- 140 direct HHs supported with seven chopper forage machines
- Number of training sessions conducted on the five areas of intervention (livestock, poultry, dairy and forage and cereal seeds) to 100% of the targeted households (based on the input each HH is receiving).
- Number of households aware of the complaints and feedback mechanism.
- Number of Baseline, PDM and Endline survey conducted.
- Number of field visits conducted
- Number of community committees established.

Table10: Outputs, activities, Sub- activities and percent achievements in the extension phase April- October 2019

Outputs	Activities	Sub-activities	Achievements (%)
Training of BFs and Distribution of Sorghum seeds to 800 beneficiaries Bait -Alfaqeeh	1. Receiving and store of 12 MT sorghum (Qaira'a verity) in Bait alfaqeeh 2. Training of beneficiaries 3. Distribution of items.	1. Starting preparation for training and distribution by making contracts with trainers. 2. Selection of distributors (Females and males) 3. Fixing the distribution points and distribution stores. 4. Conducting the training and distribution activity	100
Training of BFs and Distribution of Sorghum seeds to 550 beneficiaries Alzaydiah	1. Receiving and store of 8 MT sorghum (Zeir verity) in Alzaydiah 2. Training of beneficiaries 3. Distribution of items.		100
Training of BFs and Distribution of Sorghum seeds to 500 beneficiaries Alsuchnah	1. Receiving and store of 7 MT sorghum (Zeir verity) in Alsuchnah 2. Training of beneficiaries 3. Distribution of items.		100
Training of BFs and Distribution of Millet seeds to 800 beneficiaries Bait -Alfaqeeh	1. Receiving and store of 4 MT Millet 2. Training of beneficiaries 3. Distribution of items.		100
Training of BFs and Distribution of Millet seeds to 550 beneficiaries Alzaydiah	1. Receiving and store of 3 MT Millet 2. Training of beneficiaries 3. Distribution of items.		100
Training of BFs and Distribution of millet seeds to 500 beneficiaries Alsuchnah	1. Receiving and store of 3 MT Millet 2. Training of beneficiaries 3. Distribution of items.		100
Training and Distribution of Cowpea seeds to 800 beneficiaries Bait -Alfaqeeh	1. Receiving and store of 4 MT Cowpea 2. Training of beneficiaries 3. Distribution of items.		100
Training of BFs and Distribution of Cowpea seeds to 550 beneficiaries Alzaydiah	1. Receiving and store of 2.75 MT Cowpea 2. Training of beneficiaries 3. Distribution of items.		100
Training of BFs and Distribution of Cowpea seeds to 500 beneficiaries Alsuchnah	1. Receiving and store of 2.5 MT Cowpea 2. Training of beneficiaries 3. Distribution of items.		100
Training of BFs and distribution of small ruminants (Sheep and goats) in Assuchnah for 60 beneficiaries As-Suchnah	1. Receiving and keeping of 300 small ruminants (Sheep and goats), 12 MT feed concentrate and 600 Bs feed blocks 2. Training of beneficiaries 3. Distribution of items		100
Training of BFs and distribution of small ruminants (Sheep and goats), feed concentrate	1. Receiving and keeping of 300 small ruminants (Sheep and goats), 12 MT feed concentrate and 600 Bs feed blocks	100	

and feed blocks in Bait alfaqeeh for 60 beneficiaries Bait alfaqeeh	2. Training of beneficiaries 3. Distribution of items		
Training of BFs and distribution of small ruminants (Sheep and goats), feed concentrate and feed blocks in Alzaydah for 60 beneficiaries Alzaydah	1. Receiving and keeping of 300 small ruminants (Sheep and goats), 12 MT feed concentrate and 600 Bs feed blocks 2. Training of beneficiaries 3. Distribution of items		100
Training of BFs and distribution of egg laying chicken, chicken feed concentrates and chicken houses in Bait Alfaqeeh for 50 beneficiaries Bait Alfaqeeh	1. Receiving and keeping of 500 egg laying chicken, chicken feed 3.5 MT concentrate and chicken houses 2. Training of beneficiaries 3. Distribution of items		100
Training of BFs and distribution of egg laying chicken, chicken feed concentrate and chicken houses in Alschnah for 50 beneficiaries Alschnah	1. Receiving and keeping of 500 egg laying chicken, chicken feed 3.5 MT concentrate and chicken houses 2. Training of beneficiaries 3. Distribution of items		100
Training of BFs and distribution of egg laying chicken, chicken feed concentrate and chicken houses in Alzaidah for 50 beneficiaries Alzaidah	1. Receiving and keeping of 500 egg laying chicken, chicken feed 3.5 MT concentrate and chicken houses 2. Training of beneficiaries 3. Distribution of items		100
The chopper machines have not been received			

7. CHALLENGES ENCOUNTERED THROUGH THE IMPLEMENTATION OF THE

- Time pressure and security and movements problems due to the ongoing escalation in Hudaidah;
- Training leaflets were very limited or came too late;
- Receiving only 4000 kg of forage seeds instead of 5000 kg; and therefore distributing 20 kg for each Beneficiary instead of 25 kg;
- Iron doors and windows are exotic for Tihamah villages;
- Some of the sheep and goats received were not according to the specification (sick and very old cases have been rejected),
- The sheep and goats received in Bait Alfaqeeh were only 68.75 % of the expected amount (275 out of 400 heads);
- Most females HHs sent family male members for training and receiving of items and not coming by themselves;
- Further distribution of Animal feed concentrate has been stopped due to infestation with storage pests;

8. LESSONS LEARNED

- For building egg laying chicken houses all the materials should be used from the Tihama environment (wood and mud materials). Iron materials are subject for rusts due to the highly rel. humidity;
- Animal feed concentrate delivered to Bait alfaqeeh and Assuchnah was heavy infested with storage pests; therefore the supplier has been asked by the FAO representative to take the amounts back to be fumigated or replaced.
- FAO representatives should check the items once more shortly before delivering (storage pest cases in animal feed concentrate and delivering of very old animals might be avoided)

9. DOCUMENTATIONS

Pictures during the implementation activists April – August 2018



Item received and stores



Training of beneficiaries



Finger stamp Male HH



Training and awareness, who are the donors and implemented agencies



Beneficiary inquiry the female distributor



Finger stamp Female HH



Seeds received and taken home



Seeds received by beneficiary



Check ID of Beneficiaries



Distribution team in Bait Alfaqeeh



Training and awareness in school



Female HH received 5 heads sheep and goats



Store received sheep and goats



Male HH received 5 heads sheep and goats



Training animal health



Check the animal health and age



A group of beneficiaries transport their animals to their village



A group of beneficiaries transport their seeds to their village

Pictures during the implementation activists September 2018 – October 2019



Meeting for forming chopper user groups for the chopper machines




Signing contracts for receiving, station and operation of chopper machines



Follow up the harvest of millets



Follow up of poultry

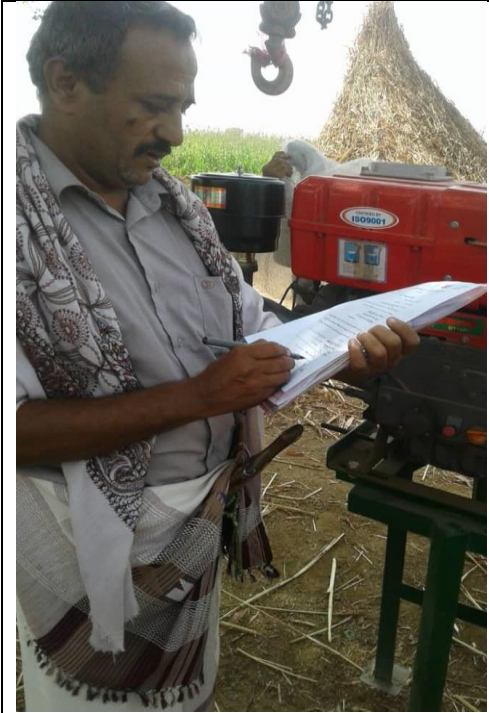

Receiving, handing over and station of chopper machines




Receiving of replaced animal feed concentrate in both districts



Distribution of the egg laying chicken



Distribution of the egg laying chicken

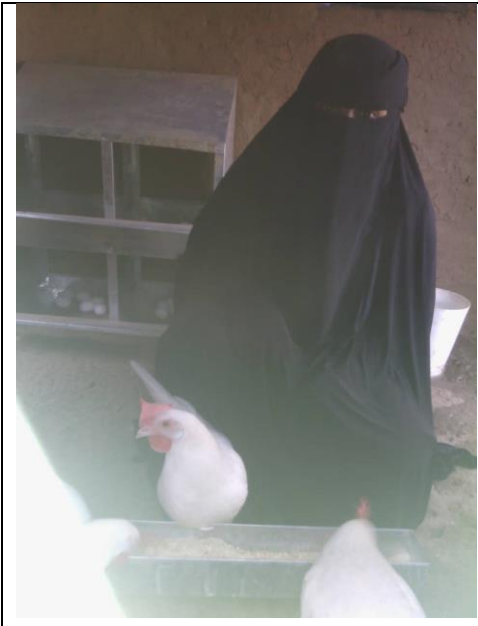

Daily collection of eggs




It is time to harvest Sorghum and millets



Training of BF's on adequate use of feed blocks



Training and awareness building of community committees leaders



Receiving, stationed and signing operation contracts of chopper machines in the first project phase

ATTACHMENTS

1. Lists of signatures or finger stamps of BFs for receiving agricultural items in the first project phase
2. Lists of signatures or finger stamps of BFs for receiving agricultural items in the extension project phase
